

LOHØGDA BORETTSLAG VÅTROMSMODERNISERING

ID	Aktivitetsnavn	Varighet	Start	Slutt	2019				2020				2021					
					Kv2	Kv3	Kv4	Kv1	Kv2	Kv3	Kv4	Kv1	Kv2	Kv3	Kv4	Kv1	Kv2	
1	Lohøgda borettslag våtromsmodernisering	667 dager	ma 04.06.18	ma 19.04.21														
2	Oppstart	0 dager	ma 04.06.18	ma 04.06.18														
3	Planlegging og rigging	45 dager	ma 04.06.18	fr 24.08.18														
4	Kjellerstreck	30 dager	ma 27.08.18	fr 05.10.18														
5	Erlendsvei 19-29 (38 bad)	45 dager	ma 08.10.18	fr 07.12.18														
6	EV 29 (6 bad)	20 dager	ma 08.10.18	fr 02.11.18														
7	EV 27 (6 bad)	20 dager	ma 15.10.18	fr 09.11.18														
8	EV 25 (6 bad)	20 dager	ma 22.10.18	fr 16.11.18														
9	EV 23 (6 bad)	20 dager	ma 29.10.18	fr 23.11.18														
10	EV 21 (6 bad)	20 dager	ma 05.11.18	fr 30.11.18														
11	EV 19 (8 bad)	20 dager	ma 12.11.18	fr 07.12.18														
12	Erlends vei 62-72 (36 bad)	45 dager	ma 07.01.19	fr 08.03.19														
13	EV 62 (6 bad)	20 dager	ma 07.01.19	fr 01.02.19														
14	EV 64 (6 bad)	20 dager	ma 14.01.19	fr 08.02.19														
15	EV 66 (6 bad)	20 dager	ma 21.01.19	fr 15.02.19														
16	EV 68 (6 bad)	20 dager	ma 28.01.19	fr 22.02.19														
17	EV 70 (6 bad)	20 dager	ma 04.02.19	fr 01.03.19														
18	EV 72 (6 bad)	20 dager	ma 11.02.19	fr 08.03.19														
19	Erlends vei 46-60 (58 bad)	55 dager	ma 18.02.19	to 09.05.19														
20	EV 46 (8 bad)	20 dager	ma 18.02.19	fr 15.03.19														
21	EV 48 (8 bad)	20 dager	ma 25.02.19	fr 22.03.19														
22	EV 50 (8 bad)	20 dager	ma 04.03.19	fr 29.03.19														
23	EV 52 (8 bad)	20 dager	ma 11.03.19	fr 05.04.19														
24	EV 54 (8 bad)	20 dager	ma 18.03.19	fr 12.04.19														
25	EV 56 (6 bad)	20 dager	ma 25.03.19	on 24.04.19														
26	EV 58 (6 bad)	20 dager	ma 01.04.19	to 02.05.19														
27	EV 60 (6 bad)	20 dager	ma 08.04.19	to 09.05.19														
28	Erlends vei 9-17 (34 bad)	36 dager	ma 15.04.19	on 12.06.19														
29	EV 9 (6 bad)	20 dager	ma 15.04.19	to 16.05.19														
30	EV 11 (6 bad)	20 dager	ti 23.04.19	on 22.05.19														
31	EV 13 (6 bad)	20 dager	ma 29.04.19	ti 28.05.19														
32	EV 15 (8 bad)	20 dager	ma 06.05.19	ti 04.06.19														
33	EV 17 (8 bad)	20 dager	ma 13.05.19	on 12.06.19														
34	Erlends vei 1-7 (28 bad)	33 dager	ma 20.05.19	fr 05.07.19														

Prosjekt: Lohøgda borettslag rev2
Dato: fr 24.08.18

Aktivitet		Milepæl		Eksterne aktiviteter	
Deling		Sammendrag		Ekstern milepæl	
Fremdrift		Prosjektsammendrag		Tidsfrist	


LOHØGDA BORETTSLAG VÅTROMSMODERNISERING

ID	Aktivitetsnavn	Varighet	Start	Slutt	2019				2020				2021		
					Kv2	Kv3	Kv4	Kv1	Kv2	Kv3	Kv4	Kv1	Kv2		
35	EV 7 (8 bad)	20 dager	ma 20.05.19	ti 18.06.19											
36	EV 5 (8 bad)	20 dager	ma 27.05.19	ti 25.06.19											
37	EV 3 (6 bad)	20 dager	ma 03.06.19	ma 01.07.19											
38	EV 1 (6 bad)	20 dager	fr 07.06.19	fr 05.07.19											
39	Erlends vei 30-44 (55 bad)	55 dager	ma 05.08.19	fr 18.10.19											
40	EK 30 (6 bad)	20 dager	ma 05.08.19	fr 30.08.19											
41	EK 32 (6 bad)	20 dager	ma 12.08.19	fr 06.09.19											
42	EK 34 (6 bad)	20 dager	ma 19.08.19	fr 13.09.19											
43	EK 36 (8 bad)	20 dager	ma 26.08.19	fr 20.09.19											
44	EK 38 (8 bad)	20 dager	ma 02.09.19	fr 27.09.19											
45	EK 40 (8 bad)	20 dager	ma 09.09.19	fr 04.10.19											
46	EK 42 (7 bad)	20 dager	ma 16.09.19	fr 11.10.19											
47	EK 44 (6 bad)	20 dager	ma 23.09.19	fr 18.10.19											
48	Erlends vei 2-28 (106 bad)	108 dager	ma 30.09.19	fr 06.03.20											
49	EK 2 (6 bad)	20 dager	ma 30.09.19	fr 25.10.19											
50	EK 4 (6 bad)	20 dager	ma 07.10.19	fr 01.11.19											
51	EK 6 (6 bad)	20 dager	ma 14.10.19	fr 08.11.19											
52	EK 8 (8 bad)	20 dager	ma 21.10.19	fr 15.11.19											
53	EK 10 (8 bad)	20 dager	ma 28.10.19	fr 22.11.19											
54	EK 12 (8 bad)	20 dager	ma 04.11.19	fr 29.11.19											
55	EK 14 (8 bad)	20 dager	ma 11.11.19	fr 06.12.19											
56	EK 16 (8 bad)	20 dager	ma 18.11.19	fr 13.12.19											
57	EK 18 (8 bad)	20 dager	ma 06.01.20	fr 31.01.20											
58	EK 20 (8 bad)	20 dager	ma 13.01.20	fr 07.02.20											
59	EK 22 (8 bad)	20 dager	ma 20.01.20	fr 14.02.20											
60	EK 24 (8 bad)	20 dager	ma 27.01.20	fr 21.02.20											
61	EK 26 (6 bad)	20 dager	ma 03.02.20	fr 28.02.20											
62	EK 28 (8 bad)	20 dager	ma 10.02.20	fr 06.03.20											
63	Kristins vei 1-21 (88 bad)	71 dager	ma 17.02.20	on 03.06.20											
64	KV 21 (8 bad)	20 dager	ma 17.02.20	fr 13.03.20											
65	KV 19 (8 bad)	20 dager	ma 24.02.20	fr 20.03.20											
66	KV 17 (8 bad)	20 dager	ma 02.03.20	fr 27.03.20											
67	KV 15 (8 bad)	20 dager	ma 09.03.20	fr 03.04.20											
68	KV 13 (8 bad)	20 dager	ma 16.03.20	on 15.04.20											

Prosjekt: Lohøgda borettslag rev2 Dato: fr 24.08.18	Aktivitet		Milepæl		Eksterne aktiviteter	
	Deling		Sammendrag		Ekstern milepæl	
	Fremdrift		Prosjektsammendrag		Tidsfrist	

LOHØGDA BORETTSLAG VÅTROMSMODERNISERING


ID	Aktivitetsnavn	Varighet	Start	Slutt	2019				2020				2021		
					Kv2	Kv3	Kv4	Kv1	Kv2	Kv3	Kv4	Kv1	Kv2		
69	KV 11 (8 bad)	20 dager	ma 23.03.20	on 22.04.20											
70	KV 9 (8 bad)	20 dager	ma 30.03.20	on 29.04.20											
71	KV 7 (8 bad)	20 dager	ti 14.04.20	ti 12.05.20											
72	KV 5 (8 bad)	20 dager	ma 20.04.20	ma 18.05.20											
73	KV 3 (8 bad)	20 dager	ma 27.04.20	on 27.05.20											
74	KV 1 (8 bad)	20 dager	ma 04.05.20	on 03.06.20											
75	Kristins vei 23-27 (32 bad)	33 dager	ma 11.05.20	ma 29.06.20											
76	KV 27 (10 bad)	20 dager	ma 11.05.20	on 10.06.20											
77	KV 25 (11 bad)	20 dager	ma 25.05.20	ma 22.06.20											
78	KV 23 (11 bad)	20 dager	ti 02.06.20	ma 29.06.20											
79	Kristins vei 2-12 (56 bad)	60 dager	ma 08.06.20	fr 18.09.20											
80	KV 2 (8 bad)	20 dager	ma 08.06.20	fr 03.07.20											
81	KV 4 (8 bad)	20 dager	ma 15.06.20	fr 10.07.20											
82	KV 6 (9 bad)	20 dager	ma 03.08.20	fr 28.08.20											
83	KV 8 (11 bad)	20 dager	ma 10.08.20	fr 04.09.20											
84	KV 10 (9 bad)	20 dager	ma 17.08.20	fr 11.09.20											
85	KV 12 (11 bad)	20 dager	ma 24.08.20	fr 18.09.20											
86	Kristins vei 14-24 (68 bad)	45 dager	ma 31.08.20	fr 30.10.20											
87	KV 14 (12 bad)	20 dager	ma 31.08.20	fr 25.09.20											
88	KV 16 (9 bad)	20 dager	ma 07.09.20	fr 02.10.20											
89	KV 18 (11 bad)	20 dager	ma 14.09.20	fr 09.10.20											
90	KV 20 (12 bad)	20 dager	ma 21.09.20	fr 16.10.20											
91	KV 22 (12 bad)	20 dager	ma 28.09.20	fr 23.10.20											
92	KV 24 (12 bad)	20 dager	ma 05.10.20	fr 30.10.20											
93	Kristins vei 26-34 (54 bad)	40 dager	ma 12.10.20	fr 04.12.20											
94	KV 34 (11 bad)	20 dager	ma 12.10.20	fr 06.11.20											
95	KV 32 (12 bad)	20 dager	ma 19.10.20	fr 13.11.20											
96	KV 30 (9 bad)	20 dager	ma 26.10.20	fr 20.11.20											
97	KV 28 (10 bad)	20 dager	ma 02.11.20	fr 27.11.20											
98	KV 26 (12 bad)	20 dager	ma 09.11.20	fr 04.12.20											
99	Kristins vei 29-37 (54 bad)	56 dager	ma 16.11.20	fr 12.02.21											
100	KV 29 (11 bad)	20 dager	ma 16.11.20	fr 11.12.20											
101	KV 31 (9 bad)	20 dager	ma 23.11.20	fr 18.12.20											
102	KV 33 (11 bad)	20 dager	ma 04.01.21	fr 29.01.21											

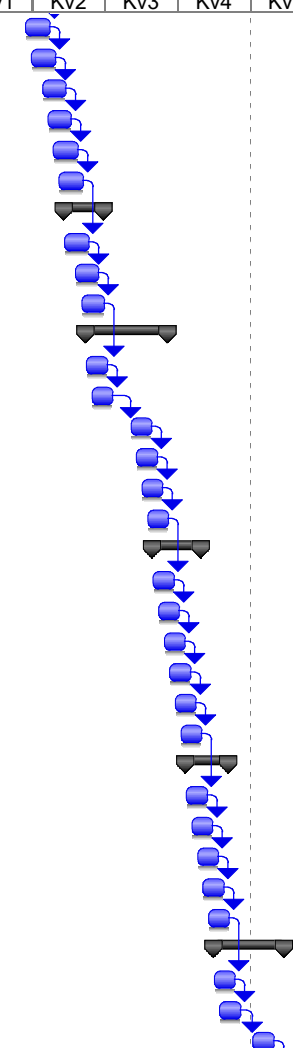

Prosjekt: Lohøgda borettslag rev2 Dato: fr 24.08.18	Aktivitet		Milepæl		Eksterne aktiviteter	
	Deling		Sammendrag		Ekstern milepæl	
	Fremdrift		Prosjektsammendrag		Tidsfrist	

LOHØGDA BORETTSLAG VÅTROMSMODERNISERING

ID	Aktivitetsnavn	Varighet	Start	Slutt	2019				2020				2021		
					Kv2	Kv3	Kv4	Kv1	Kv2	Kv3	Kv4	Kv1	Kv2		
103	KV 35 (12 bad)	20 dager	ma 11.01.21	fr 05.02.21											
104	KV 37 (11 bad)	20 dager	ma 18.01.21	fr 12.02.21											
105	Kristins vei 39-43 (27 bad)	30 dager	ma 25.01.21	fr 05.03.21											
106	KV 43 (9 bad)	20 dager	ma 25.01.21	fr 19.02.21											
107	KV 41 (9 bad)	20 dager	ma 01.02.21	fr 26.02.21											
108	KV 39 (9 bad)	20 dager	ma 08.02.21	fr 05.03.21											
109	Kristins vei 36-42 (43 bad)	33 dager	ma 15.02.21	on 31.03.21											
110	KV 36 (11 bad)	20 dager	ma 15.02.21	fr 12.03.21											
111	KV 38 (11 bad)	20 dager	ma 22.02.21	fr 19.03.21											
112	KV 40 (9 bad)	20 dager	ma 01.03.21	fr 26.03.21											
113	KV 42 (12 bad)	18 dager	ma 08.03.21	on 31.03.21											
114	Nedrigging	10 dager	ti 06.04.21	ma 19.04.21											
115	Ferdig	0 dager	ma 19.04.21	ma 19.04.21											



Prosjekt: Lohøgda borettslag rev2
 Dato: fr 24.08.18

Aktivitet		Milepæl		Eksterne aktiviteter	
Deling		Sammendrag		Ekstern milepæl	
Fremdrift		Prosjektsammendrag		Tidsfrist	
